

MAYVILLE STATE UNIVERSITY


Old Main Renovation

Jobsite Newsetter

Get the latest updates on the renovation of Mayville State's historic Old Main! Follow progress, upcoming projects, and more as PCL/Community Contractors work to preserve its legacy and shape its future.

PROGRESS UPDATES

- **Basement:** Work continues to take shape with lighting installation and ceiling cloud veneer underway. Theater seating and theater lighting are next, with installation expected to begin in the coming weeks.
- **First floor:** Punch list work in progress
- **Second floor:** Punch list work in progress
- **Third floor:** Punch list work in progress
- **Fourth floor:** Punch list work in progress

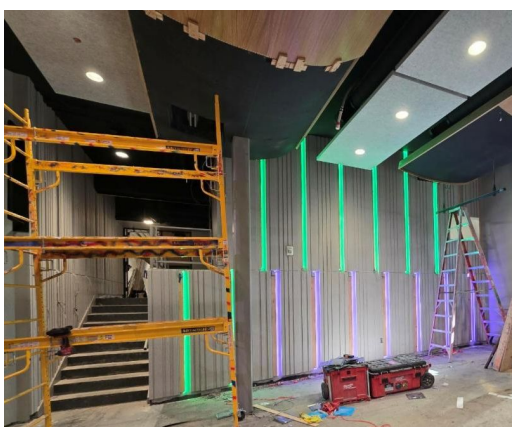

The lights are on in the theater, bringing the space one step closer to completion.



Tile installation is complete in Stair 1 through the third floor, while mudding and taping continue on the upper levels.



Signage installation is underway, along with the reinstallation of the original ticket booth millwork.

UPCOMING WORK

Finishes are progressing throughout the theater as the team works toward completing the remaining work in the east half of the building.

DID YOU KNOW?

The theater uses different types of acoustical treatments to help control how sound travels through the space. Some absorb sound, while others help reflect and distribute it. Seeing these elements come together is an exciting part of the theater's transformation.

QUALITY CORNER

Precision is especially important when installing the theater's acoustical panels. The seams between the 2-inch and 4-inch panels need to align consistently up and down the walls, making careful layout and installation key to achieving a clean finished appearance.

SAFETY TOPIC

The theater's sloped seating presented a unique challenge while crews worked on the overhead ceiling clouds. To create a safe, level working surface for scaffolding, the team used mud sills at varying heights to account for the slope.

PCL CONSTRUCTION | COMMUNITY CONTRACTORS INC.
A JOINT VENTURE

Mayville State University

FOSS ARCHITECTURE +INTERIORS

This project is funded through appropriates made by the North Dakota 68th Legislative Assembly.

October 2026
